

73rd MORSS CD Cover Page

UNCLASSIFIED DISCLOSURE FORM CD Presentation

712CD

For office use only 41205

21-23 June 2005, at US Military Academy, West Point, NY

Please complete this form 712CD as your cover page to your electronic briefing submission to the MORSS CD. Do not fax to the MORS office.

Author Request (To be completed by applicant) - The following author(s) request authority to disclose the following presentation in the MORSS Final Report, for inclusion on the MORSS CD and/or posting on the MORS web site.

Name of Principal Author and all other author(s): Dr. William Jarvis

Principal Author's Organization and address:

OSD CAIG

1800 Defense Pentagon, Room BE-779

Washington, DC. 20301-1800

Phone: 703-695-7282

Fax: 703-692-8054

Email: wjarvis@comcast.net

Original title on 712 A/B: Office of the Secretary of Defense (PA&E)

Revised title: Patterns of Resource Expenditure

Presented in (input and Bold one): (WG 27, CG____, Special Session ____, Poster, Demo, or Tutorial):

This presentation is believed to be:

UNCLASSIFIED AND APPROVED FOR PUBLIC RELEASE

Report Documentation Page				Form Approved OMB No. 0704-0188	
Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.					
1. REPORT DATE 22 JUN 2005		2. REPORT TYPE N/A		3. DATES COVERED -	
4. TITLE AND SUBTITLE Patterns of Resource Expenditure				5a. CONTRACT NUMBER	
				5b. GRANT NUMBER	
				5c. PROGRAM ELEMENT NUMBER	
6. AUTHOR(S)				5d. PROJECT NUMBER	
				5e. TASK NUMBER	
				5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) OSD CAIG 1800 Defense Pentagon, Room BE-779 Washington, DC. 20301-1800				8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)				10. SPONSOR/MONITOR'S ACRONYM(S)	
				11. SPONSOR/MONITOR'S REPORT NUMBER(S)	
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release, distribution unlimited					
13. SUPPLEMENTARY NOTES See also ADM201946, Military Operations Research Society Symposium (73rd) Held in West Point, NY on 21-23 June 2005. , The original document contains color images.					
14. ABSTRACT					
15. SUBJECT TERMS					
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT UU	18. NUMBER OF PAGES 30	19a. NAME OF RESPONSIBLE PERSON
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified			




Patterns of Resource Expenditure

Will Jarvis
OSD PA&E



Overview

- Problem
- Unconstrained Resource Allocation
 - Beta Curve
 - Rayleigh Curve
 - Sech² Curve
 - Sine Curve (New!)
- Summary and Conclusions

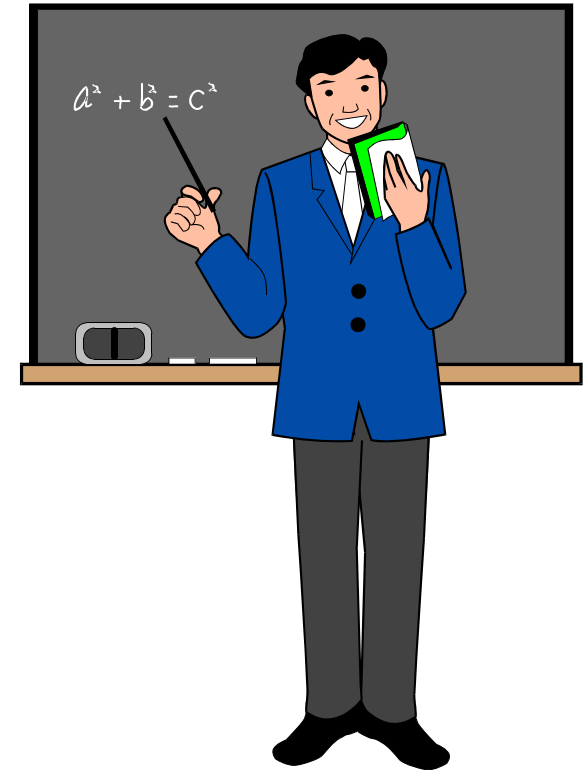

Introduction

- Rate of progress on a project is affected by dependencies among the problems being solved. For example,
 - Some problems cannot be worked until others are finished.
 - Some problems can be worked simultaneously.
 - New problems may surface as old ones are being worked.

Introduction

- If a project ramps up too quickly to maximum loading, then resources are wasted before work is really uncovered and available for doing.
- If a project ramps up too slowly then budget overruns occur late in the project as timelines are compressed.
- Is there an optimum way to allocate resources to a project?


Introduction

- We examine four methods of resource allocation:
 - Beta Curve
 - Rayleigh Model
 - Sech² Model
 - Sine Model (New!)

Beta

- The beta curve is often used to empirically fit manpower patterns,

$$\frac{dW(t)}{dt} = \frac{\Gamma(a+b)}{\Gamma(a)\Gamma(b)} t^{a-1} \bullet (1-t)^{b-1} \quad 0 < t < 1$$

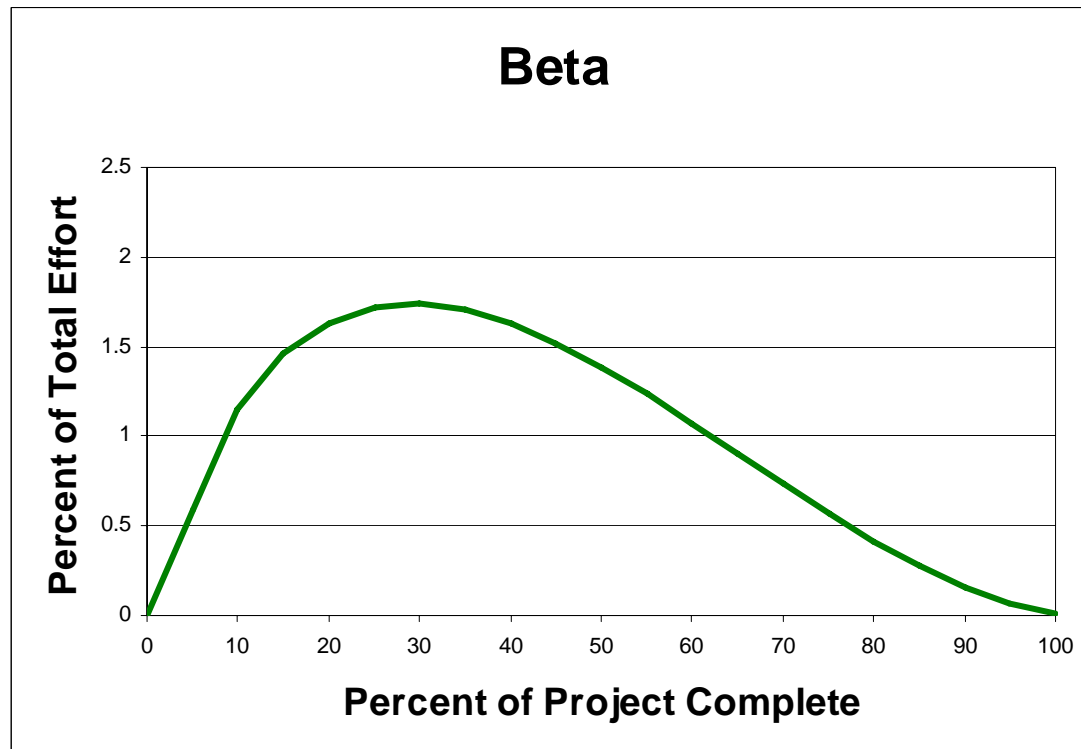

Beta

- The beta curve provides great flexibility; however, a theoretical justification for use of the curve is lacking.
- Norden introduced the Rayleigh curve, asserting that a project is a set of unsolved problems.
- Later Parr, introduced the notion of *visible* unsolved problem space.

Rayleigh Model

- A project involves solving some fixed number of problems.
- The rate at which problems are solved is jointly proportional to (1) the level of skill available, $p(t)$; and (2) the fraction of problems left to solve.

$$\frac{dW(t)}{dt} = p(t) \bullet (1 - W(t))$$

- On integration,

$$W(t) = 1 - \exp\left(-\int^t p(\tau) d\tau\right) \quad \text{Eqn. R1}$$

Rayleigh Model

- Assume a linear learning rate.

$$p(t) = \alpha \cdot t \quad \text{Eqn. R2}$$

- The Rayleigh curve follows (*substitute Eqn R2 into Eqn R1, then differentiate*).

$$\frac{dW(t)}{dt} = \alpha \cdot t \cdot \exp\left[-\frac{\alpha \cdot t^2}{2}\right] \quad \text{Rayleigh Curve}$$

Rayleigh Model

- “Spreading” an Estimate

- Time of Peak Staffing is close to development time, so let

$$\left(\frac{d^2 W(t)}{dt^2} \right)_{t=t_d} = -\alpha^2 t_d^2 e^{-\frac{\alpha t_d^2}{2}} + \alpha e^{-\frac{\alpha t_d^2}{2}} = 0$$

- Solving for α , we get,

$$\alpha = \frac{1}{t_d^2}$$


- For the Rayleigh distribution, the peak occurs at the 39th percentile so,

$$K = \frac{E}{0.39}$$

Rayleigh Model

- In terms of development time (t_d) and total effort (E), resource consumption is expressed as,

$$\frac{dW(t)}{dt} = \frac{E}{0.39} \bullet \left(\frac{1}{t_d^2} \cdot t \cdot \exp \left[-\frac{t^2}{2 \cdot t_d^2} \right] \right)$$

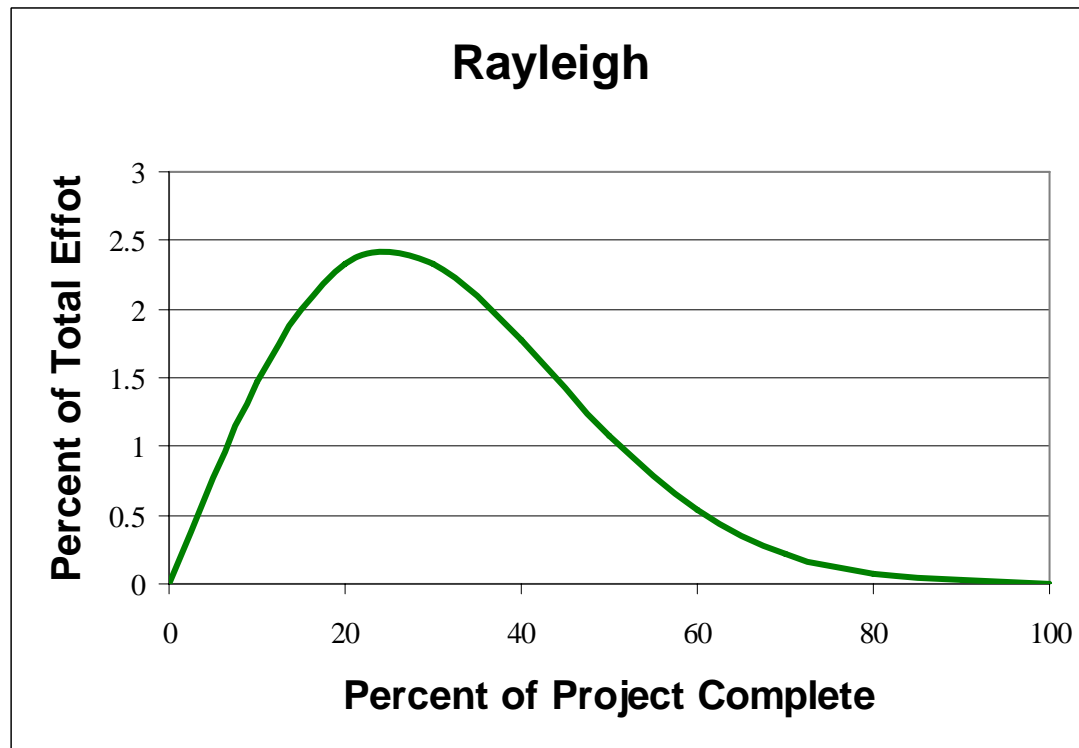

Rayleigh Model

- Main assumptions of Putnam-Norden Rayleigh Model:
 - Initial ramp-up is due to a linear learning curve.
 - Exponential tail-off is due to exhaustion of the problem space -- that is, the rate at which work is done is proportional to the amount of work left.
- Parr criticizes Putnam and Norden's first assumption, arguing that it "confuses intrinsic constraints" on the rate at which work can be accomplished with "management's economically governed choices on how to respond to these constraints".

Parr Sech² Model


- Let $W(t)$ = *proportion of problems which have been solved*, as with the Putnam Norden Model.
- Introduce $V(t)$ = *proportion of visible unsolved problems*.
- Parr asserts that the rate of progress on a project is governed by dependencies among the problems that must be solved.
 - Some problems must be solved in sequential order.
 - Other problems can be solved in parallel.

Parr Sech² Model

- If we consider a short time interval that encloses the solution of just one problem, then it is immediate that

$$W(t^+) = W(t^-) + 1$$

- Now, Parr assumes that the dependency relation among problems is a binary tree. That is, the solution of a problem leads to no further problems, or else leads to two new problems.



Parr Sech² Model

- In equation form,

$$V(t^+) = V(t^-) + 1 \quad \text{if problem has dependents}$$

$$V(t^+) = V(t^-) - 1 \quad \text{if problem has no dependents}$$

- Second assumption:

- “... the probability that the most recently solved problem has no dependents is linear in the number of problems solved.”

- In equation form, this becomes

$$V(t^+) = V(t^-) + 1 \quad \text{with probability } 1 - \frac{W(t^-)}{N}$$

$$V(t^+) = V(t^-) - 1 \quad \text{with probability } \frac{W(t^-)}{N}$$

N is the total number of problems to be solved.

Parr Sech² Model

- Taking expectations yields,

$$E[V(t^+)] = V(t^-) + 1 - 2 \frac{W(t^-)}{N}$$

- In words: *The expected change in the number of visible problems decreases linearly with the work completed.*
- Each time a problem is solved, we expect the size of the visible problem space to grow as

$$\Delta V(t) = 1 - 2W(t)$$

N disappears
through
normalization.

Parr Sech² Model

- Now, given that the rate at which problems are solved is $dW(t)/dt$, then

$$\frac{dV(t)}{dt} = \frac{dW(t)}{dt} \cdot (1 - 2W(t)) \quad \text{Eqn. S1}$$

- In words: *The rate of change in the number of visible unsolved problems is jointly proportional to (1) the rate of solving problems; and (2) the expected change in the number of visible unsolved problems per problem solved.*

Parr Sech² Model

- Parr's second assertion is that “the rate at which work can be usefully input ... is proportional to $V(t)$.”
- In equation form,


$$\frac{dW(t)}{dt} = \alpha \cdot V(t)$$

Eqn. S2

Parr Sech² Model

- Solution, found by solving Eqns S1 and S2, is

$$V(t) = \frac{A \exp(-\alpha t)}{(1 + A \exp(-\alpha t))^2} = \frac{1}{4} \cdot \operatorname{sech}^2\left(\frac{(\alpha t + c)}{2}\right)$$

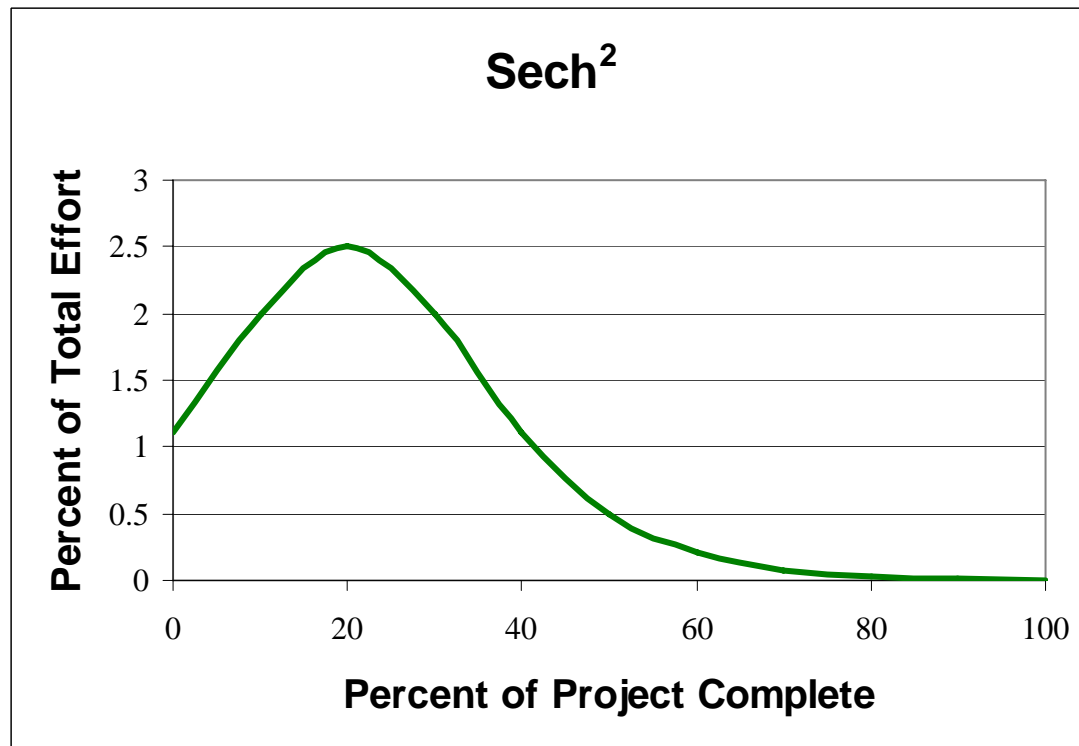

Sine Model

- As before,
 - Let $W(t)$ = *proportion of problems which have been solved*, (same as Putnam-Norden Model).
 - Let $V(t)$ = *proportion of visible unsolved problems*.
- Two assumptions:
 - Rate at which problems are uncovered is proportional to the difference between (a) the amount of work remaining, and (b) the amount of visible unsolved problems.
 - Rate at which problems are solved is proportional to the number of visible unsolved problems.

Sine Model

- In equation form, our assumptions can be restated as

$$\dot{V} = (1 - W) - V$$

$$V = \dot{W}$$

For clarity, the constants of proportionality are omitted.

- Differentiating the first equation further, we get

$$\ddot{V} = -\dot{W} - \dot{V}$$

$$V = \dot{W}$$

- Together, these two equations yield

$$\ddot{V} + \dot{V} + V = 0$$

Sine Model

- The general solution is of the form,

$$V = e^{-\alpha t} (C_1 \cos bt + C_2 \sin bt)$$

Constants α and b are functions of proportionality constants in original set of differential equations.

- With the constraint that $V(0) = 0$, then the general solution reduces to

$$V = e^{-\alpha t} \sin bt$$

Later, we normalize the solution. So for now, we can set $C_2 = 1$, without loss in generality.

- As with the Rayleigh, we associate the time of peak staffing, with the end of the development phase (t_{dev}). So,

$$\dot{V} = -\alpha e^{-\alpha t_d} \sin bt_{dev} + b e^{-\alpha t} \cos bt_{dev} = 0$$

Sine Model

- Solution of this equation yields

$$\alpha = b \frac{\cos bt_{dev}}{\sin bt_{dev}}$$

- Now, we introduce a project endpoint as t_{end} . We require that

$$V(t_{end}) = e^{-\alpha t_{end}} \sin bt_{end} = 0$$

or

$$\sin bt_{end} = 0$$

or

$$b = n \frac{\pi}{t_{end}}$$

For our purpose, $n = 1$.

Sine Model

- The normalization factor is derived as,

$$C = \int_0^{t_{end}} V \cdot dt$$

$$= \int_0^{t_{end}} e^{-\alpha t} \sin bt \cdot dt$$

$$= \frac{e^{-\alpha t_{end}} (\alpha \sin bt_{end} - b \cos bt_{end}) + b}{\alpha^2 + b^2}$$

Sine Model

- The solution is now expressed in terms of project effort (E manmonths), development time (t_{dev}), project end-time (t_{end}):


$$V = \frac{E}{C} e^{-\alpha t} \sin bt$$

where,

$$b = \frac{\pi}{t_{end}}$$

$$\alpha = b \frac{\cos bt_{dev}}{\sin bt_{dev}}$$

Sine Model

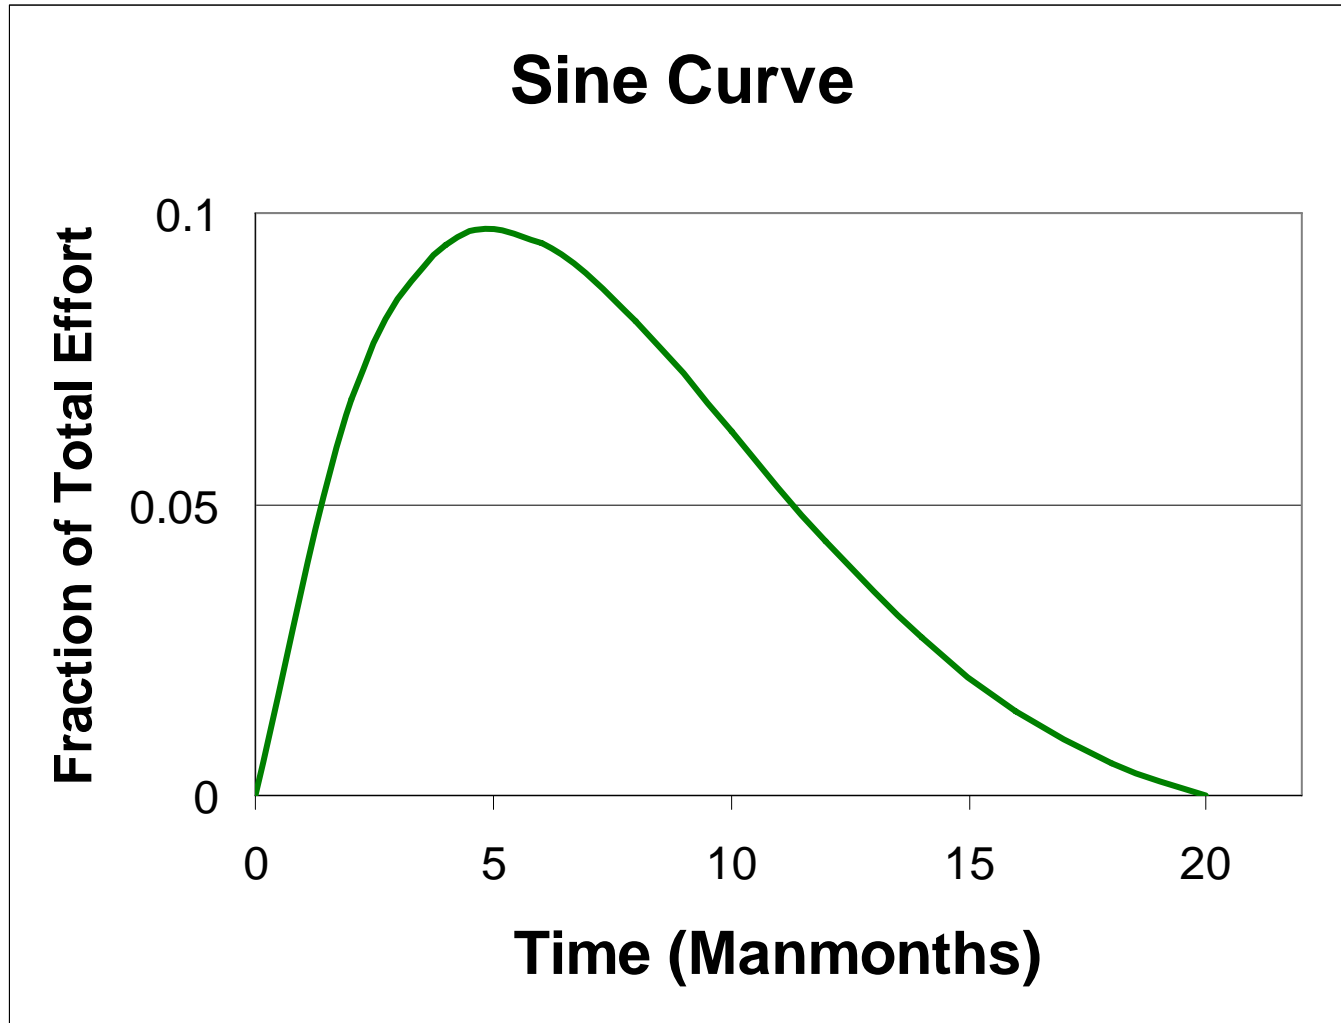

Conclusions

- The Beta curve is a useful tool for fitting manpower patterns. However, it offers little understanding of how a problem-solving process behaves.
- The Rayleigh curve presumes a linear pattern of manpower buildup. It offers some understanding of how the process behaves once peak staffing occurs.
- For the Rayleigh, Sech², and Sine models, the decay in work rate is due to exhaustion of the problem space.

Conclusions

- In the Sech² and Sine models, resource allocation is fully unconstrained in the sense that program managers apply large amounts of input resources whenever there exists the potential for solving problems in parallel. In the Rayleigh model, resource allocation is linearly constrained during the buildup.
- Both the Rayleigh and Sech² curves have infinite tails, making them awkward to use in practice. The Sine curve does not have infinite tails.
- The Rayleigh, Sech², and Sine curves offer insight into when we should expect peak resource expenditure to occur for any given project.

Next Steps

- Normalize all models, compare side-by-side.
- Evaluate alternative initial conditions.
 - Does changing the proportion of problems that are visible at the start of the project affect when peak staffing occurs?
- Degrees of Freedom (e.g., time of peak Rayleigh vs. duration is a fixed ratio).
